

# Juvenile & Domestic Relations District Court Update

*October 12, 2023*

*Presented by The Department of Public Works*

# Agenda

- Schedule Review
- Schematic Design
- Next Steps

# Court Order Milestones

## Schematic Design

- ✓ Submitted by August 16
- ✓ Approved by October 2

## Developmental Design

- Submitted by November 22
- Approved by December 13

## Final Construction Documents


- Ready by January 15

## Construction


- Begins by April 18, 2024
- Complete by November 1, 2025





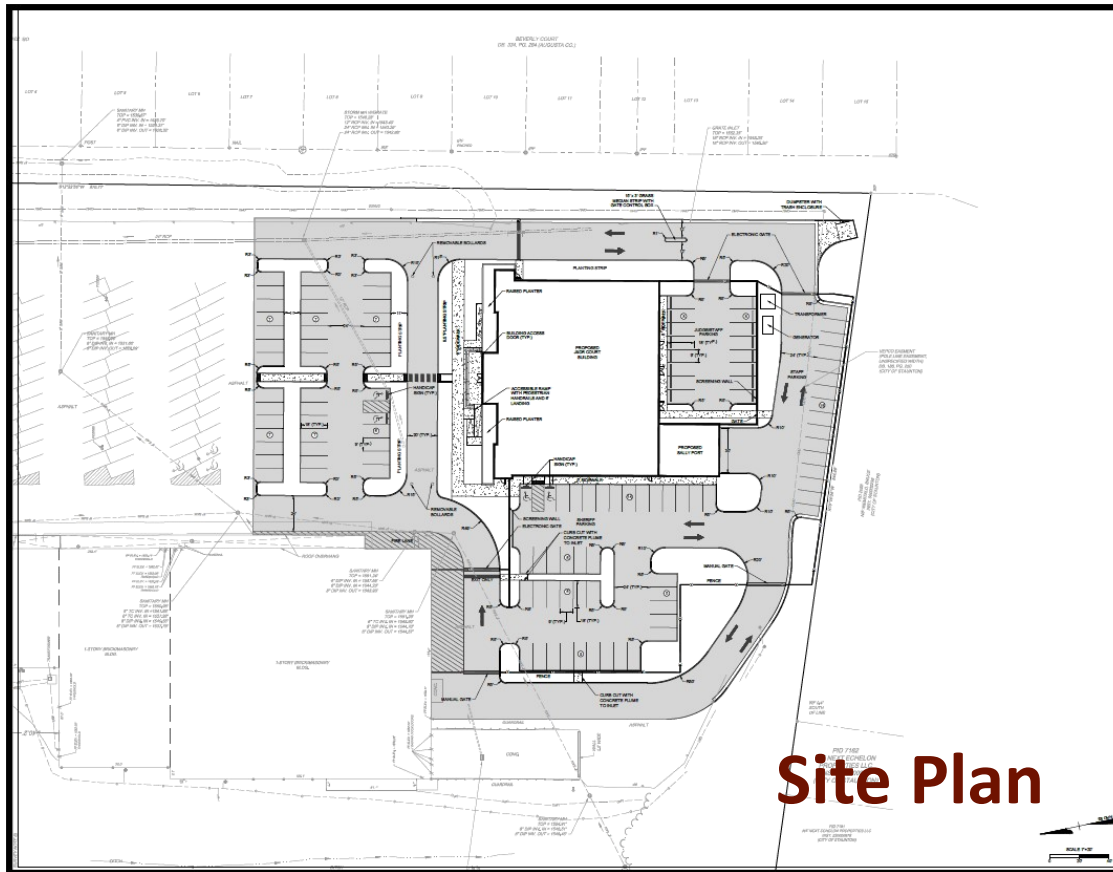

# Site Plan

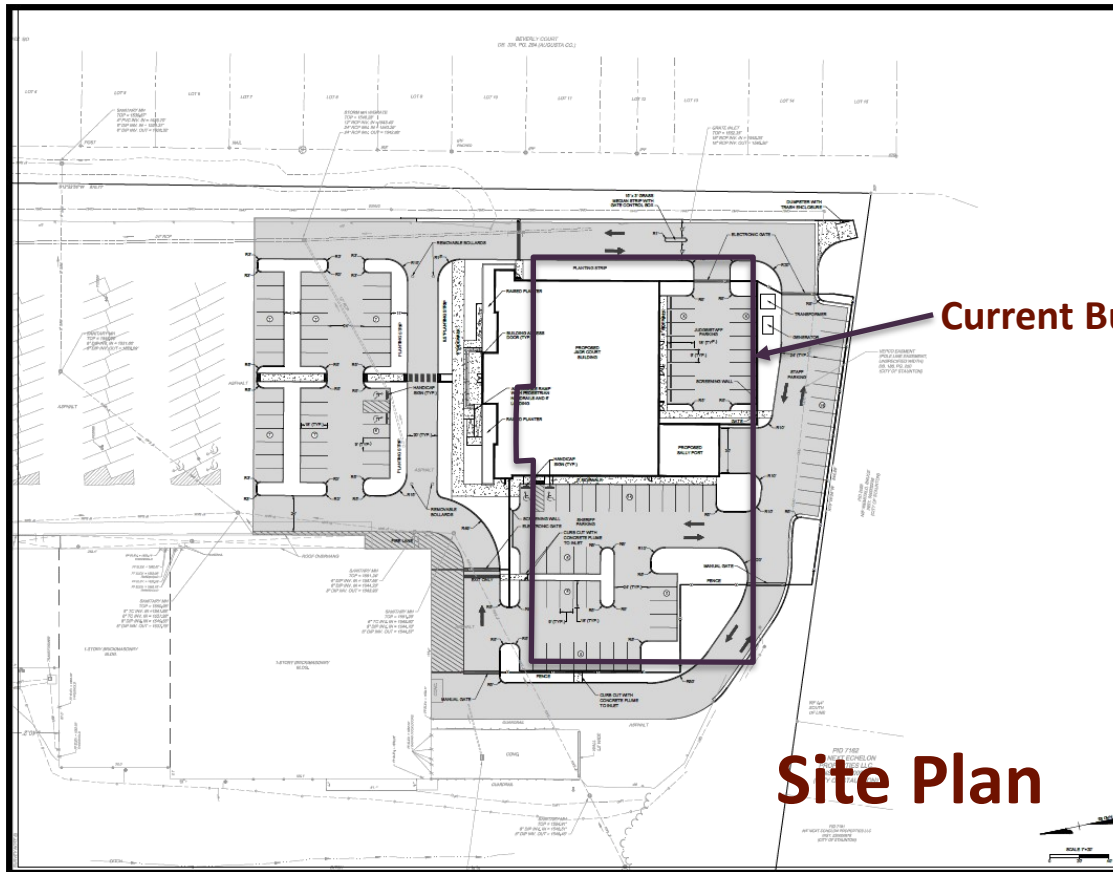

Current Building

Site Plan





# Next Steps

## Developmental Design

- Security Plan
- IT Plan
- Site Plan

## Demolition Plan

- Separate contract?

## Overall Site Master Plan

- Initial data collection underway
- Roof contract in development

# Questions?
